

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

Student Project Portfolio & Showcase App

Name	Bharat V Bhat
SRN	PES1UG24CS113
Section	B
Course	UE24CS341A : Software Engineering
Domain	Campus & Academic Operations
Problem Statement	#04 - Student Project Portfolio & Showcase App
Jira Project / Workspace	https://bharatvbhat2006.atlassian.net/jira/software/c/projects/SPPSA/summary

This report contains the required Jira evidence, sprint analytics and reflection answers.



1. Epics & User Stories / Backlog

The List view shows the four Epics and their seven User Stories, along with priority, status and story points.

☐	Work	Priority	Status	Due date	Story Points	
☐	✦ SPPSA-1 Project Showcase & Submission	Medium	To Do	None	None	...
☐	☑ SPPSA-5 Create Showcase Profile	High	Done	None	5	...
☐	☑ SPPSA-6 Upload Multimedia Artifacts	Medium	Done	None	3	...
☐	✦ SPPSA-2 Project Evaluation	Medium	To Do	None	None	...
☐	☑ SPPSA-7 Grade Project	High	Done	None	5	...
☐	✦ SPPSA-3 Public Voting	Medium	To Do	None	None	...
☐	☑ SPPSA-8 Cast Public Vote	High	Done	None	3	...
☐	☑ SPPSA-9 Verify Voter	High	Done	None	5	...
☐	✦ SPPSA-4 Results & Leaderboard	Medium	To Do	None	None	...
☐	☑ SPPSA-10 View Leaderboard	Medium	Done	None	3	...
☐	☑ SPPSA-11 Real-Time Leaderboard Updates	High	Done	None	8	...
+ Create 4 of 4 ↺						



2. User Story Details

Example captured Jira story details for Create Showcase Profile. The screenshots show the story description, priority, story points, and parent Epic.

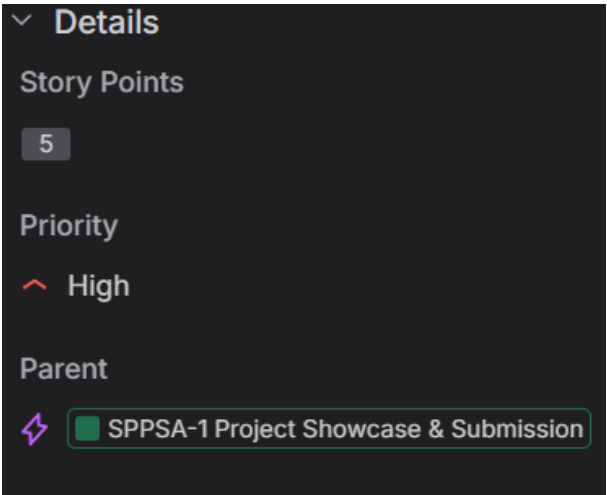


3. Sprint Execution - Sprint 1

The following screenshots record the progression of Sprint 1 from the initial board state to completed work.

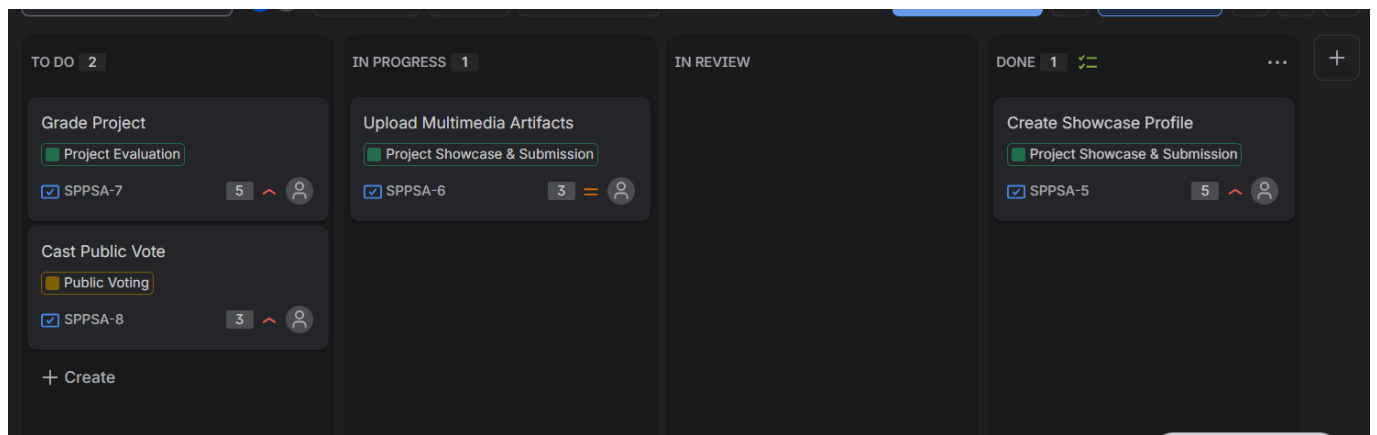

4. Sprint Execution - Completion


Sprint 1 work was moved through the board until all four selected stories were completed.

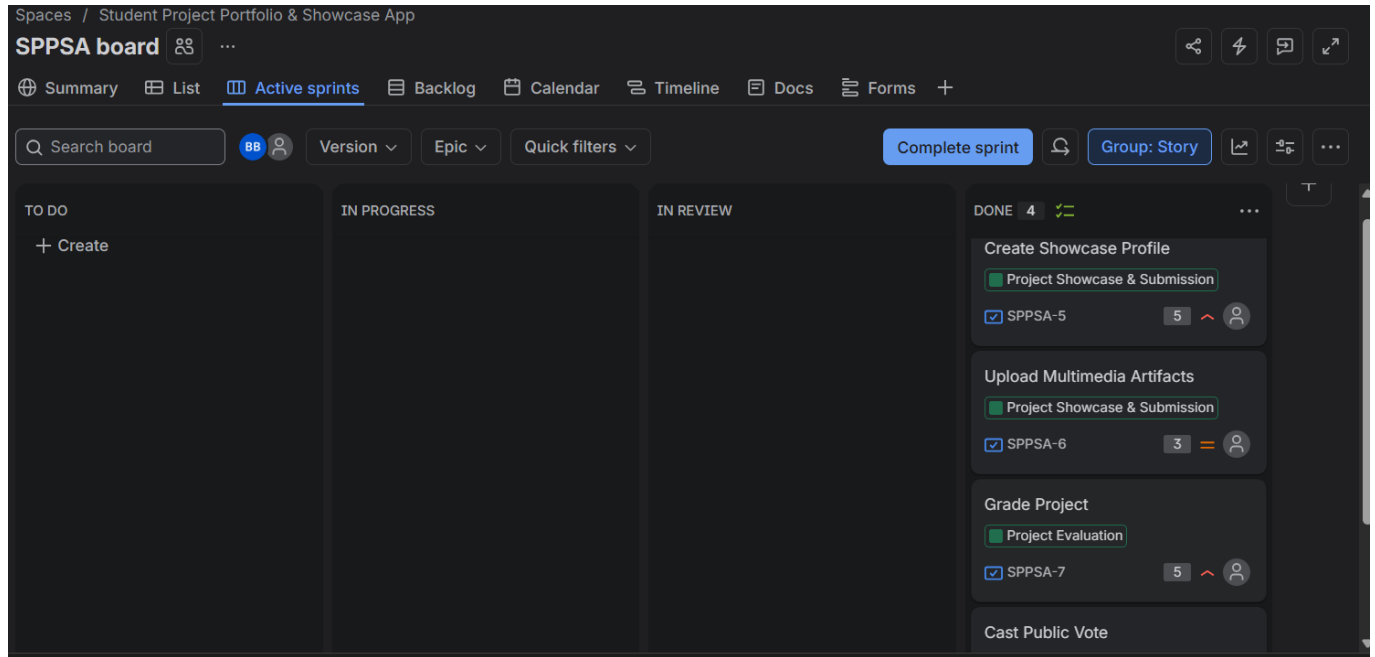

Sprint 1 scope: Create Showcase Profile (5), Upload Multimedia Artifacts (3), Grade Project (5), and Cast Public Vote (3) — 16 points total.

5. Final Sprint State


After Sprint 2, Jira created an empty Sprint 3. The three remaining Sprint 2 stories were completed, so no third sprint was run.

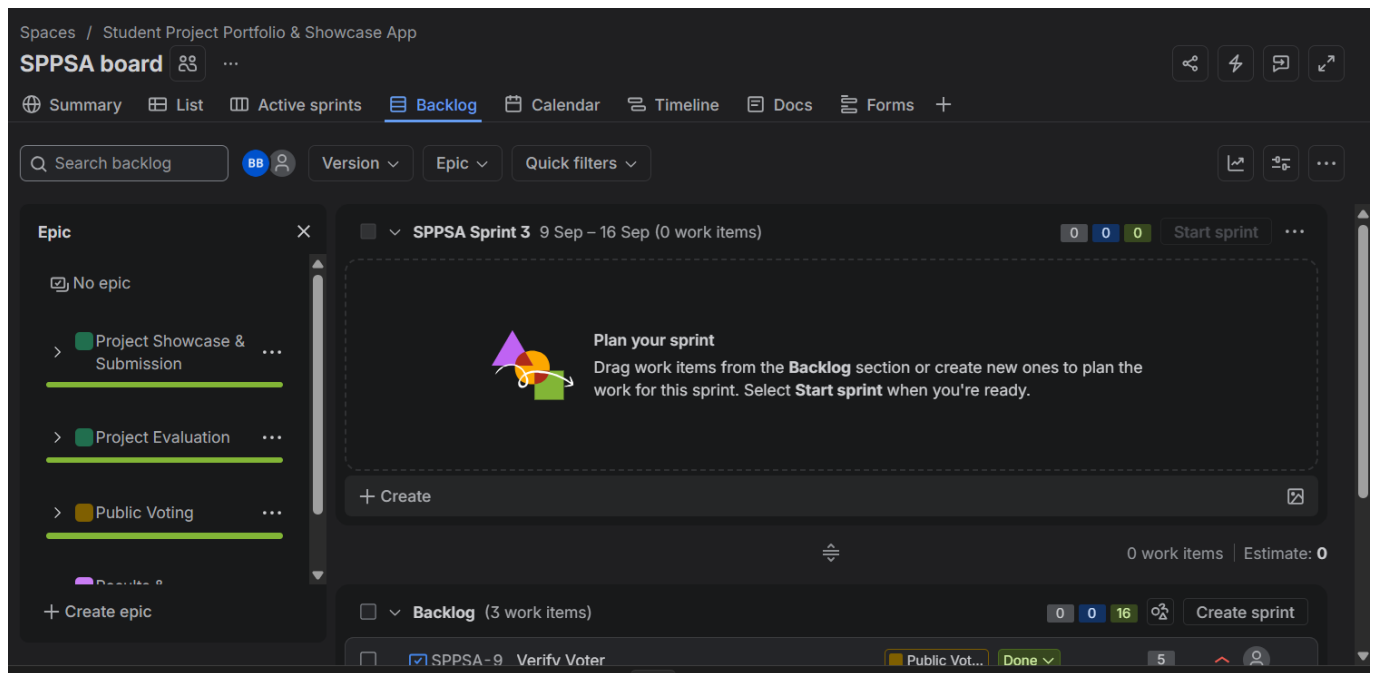

Two sprints were completed as required: Sprint 1 and Sprint 2.

6. Jira Summary / Analytics


The Jira Summary page provides a quick visual view of work items by status, type, and assignee. This is supplementary evidence for the completed Jira workspace.

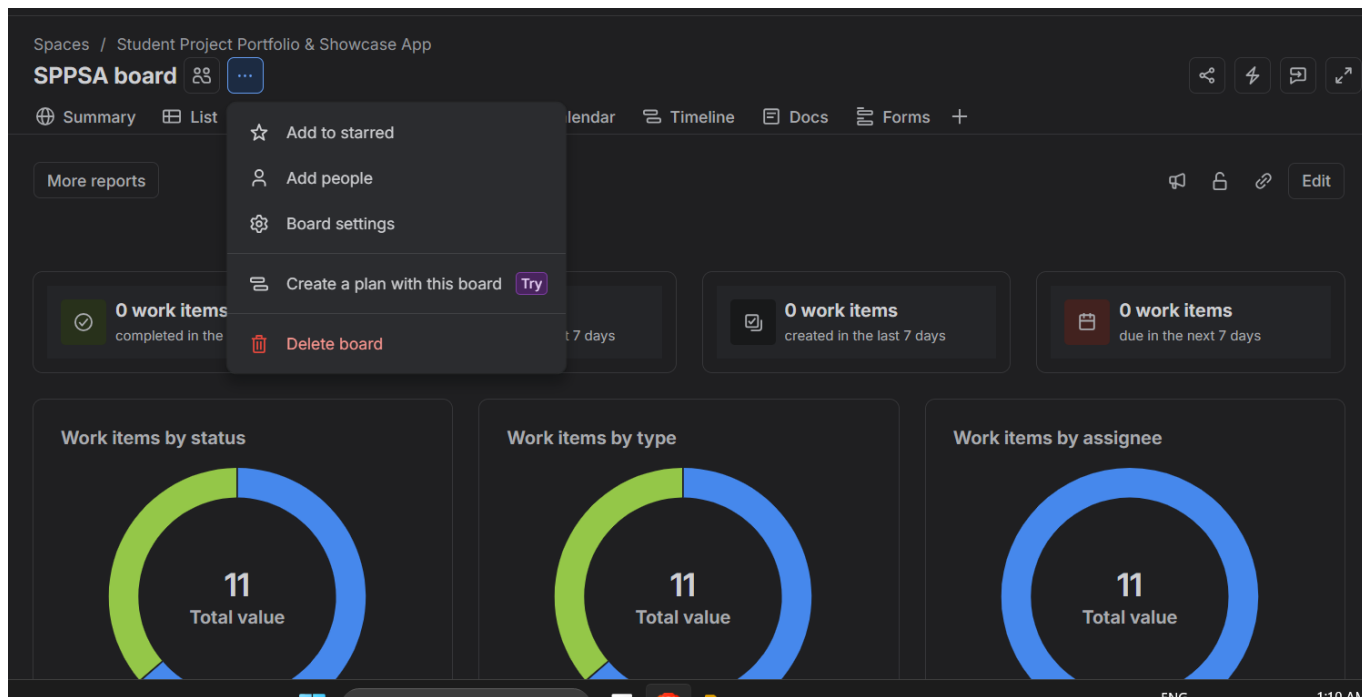

The dashboard shown here was captured from the SPPSA board after the sprint work had been completed.

7. Sprint Analytics - Burndown Chart

Sprint 1 is plotted using Story Points. The planned workload started at 16 points and reached 0 as the four stories were completed.

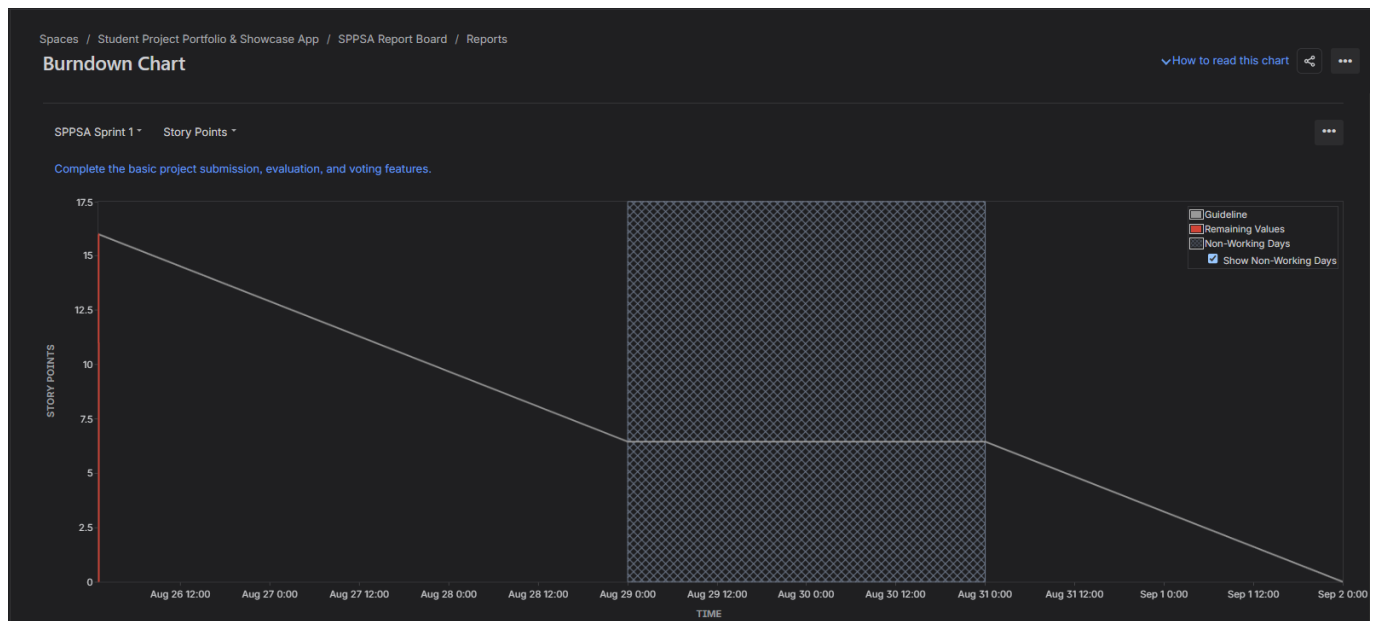

8. Burndown Event Details

The event table records the Sprint 1 burn-down sequence: 16 → 11 → 8 → 3 → 0 remaining Story Points.

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
26/Aug/26 12:57 AM	SPPSA-5	Sprint start		5		
	SPPSA-6			3		
	SPPSA-7			5		
	SPPSA-8			3		
	Total					16
26/Aug/26 12:59 AM	SPPSA-5	Burndown	Issue completed		5	11
26/Aug/26 1:00 AM	SPPSA-6	Burndown	Issue completed		3	8
	SPPSA-7	Burndown	Issue completed		5	3
	SPPSA-8	Burndown	Issue completed		3	0
26/Aug/26 1:02 AM	SPPSA-5	Sprint ended by Bharat bhat				0
	SPPSA-6					0
	SPPSA-7					0
	SPPSA-8					0
	Total					0

9. Reflection Answers

1. Did your estimations reflect the actual effort?

I think the estimates were reasonable for the simulation. Smaller items were given 3 points, while the more involved stories were given 5 points. Real-time leaderboard updates got 8 points because they had more complexity and uncertainty. Since this was only a simulation, the points were mainly used to compare relative effort.

2. Was your backlog well-prioritized?

Yes. The main features needed for the system were given High priority, such as profile creation, grading, voting and voter verification. Uploading artifacts and viewing the leaderboard were kept at Medium because they were important, but not as critical as the core flow.

3. How did your simulated sprint align with your plan?

The work was split into two one-week sprints. Sprint 1 had four stories and Sprint 2 had the remaining three. All the selected stories were moved to Done by the end of the two sprints, so the planned work was completed.

4. What insights did the burndown chart give about your team's capacity?

The Sprint 1 burndown started at 16 story points and dropped to 11, 8, 3 and finally 0 as the stories were completed. This shows that the team finished the planned Sprint 1 work within the simulated sprint. It also gives a rough idea of the amount of work the team was able to handle in one sprint.

Jira Project / Workspace: <https://bharatvbhat2006.atlassian.net/jira/software/c/projects/SPPSA/summary>
